<u>Civil Works Program and Budget Process-Section 4Civil Works Program</u> <u>Budget Cycle – Defense of President's Budget</u>

Scope

This process provides guidance for development and submission of the budget for the U.S. Army Corps of Engineers, Civil Works program.

- Saving a budget type in P3e will automatically trigger the P3e-Oracle Projects interface to pass "President's Budget" budget-type to Oracle Projects. P2 will notify the Program Analyst that the "President's Budget" budget-type has been sent to Oracle Projects.
- Once PM does recommended plan, then project is fit into ceiling and adjustments need to be made back to PM.

Policy

<u>EC 11-2-18x[http://www.usace.army.mil/inet/usace-docs/eng-circulars/ec-cw.html]</u> (Note: The EC increases by one number each fiscal year. The EC includes a list of all applicable public laws, Executive orders, Army regulations, Engineer Regulations, Engineer Pamphlets, Engineer Manuals, and other policy guidance relevant to the budget year under development.)

ER 11-2-201, Civil Works Activities – Funding, Work Allowances, and Reprogramming

Related Processes System References

Activity Development[PROC1010]

CEMRS Home Page[http://www.usace.army.mil/inet/functions/rm/manpower/requirements/]

<u>Civil Works O&M Automated Budget System (ABS) Home</u> Page[http://www.cecer.army.mil/abs/default.asp]

Civil Works Program and Budget Process[PROC1022]

Civil Works Program and Budget Process-Section 1[PROC1027]

Civil Works Program and Budget Process-Section 2[PROC1028]

Civil Works Program And Budget Process-Section 3[PROC1029]

<u>Civil Works Program and Budget Process-Section 5[PROC1031]</u>

District Operating Budget[PROC1015]

Initiating a Project in P2[PROC1005]

Copyright Oracle Corporation, 2000. All rights reserved.

PMP/PgMP Content[REF1018]

Resource Estimate Development[PROC1003]

Responsibility

The Program Managers (PgMs) in HQUSACE, MSCs, and districts are responsible for integrating and developing the Civil Works annual budget request, preparation of budget testimony, interfacing with Congressional committees, program/project management policy and guidance, and program management and performance

The Chief of Engineers is responsible for testifying before the House and Senate Appropriation sub-committee hearings.

Distribution

Chief of Engineers*

District Program Manager (PgM)*

Headquarters (HQUSACE) Program Manager (PgM)*

Major Subordinate Command (MSC) Program Manager (PgM)*

District Project Manager

District Program Analysist

Ownership

The <u>BP/P2 Program OfficeConfiguration Management Board</u> is responsible for ensuring that this document is necessary, that it reflects actual practice, and that it supports corporate policy.

Copyright Oracle Corporation, 2000. All rights reserved.

Activity Preface

This process runs concurrently with the PDT processes. The level of detail defined in PMP/PgMP Content[REF1018] will provide guidance for such items as activity/resource estimate development (refer to Activity Development [PROC1010], and Resource Estimate Development[PROC1003].

Chief of Engineers

Testify before House and Senate Appropriation sub-committee hearings on President's budget request.

Headquarters (HQUSACE) Program Manager (PgM)

2. Provide requests for Congressional member fact sheets to MSCs and responsible Districts.

District Program Manager (PgM)

- Prepare Congressional member fact sheets, in coordination with PM, for Congressional members' requests to HQUSACE for submission to the Sub-Committee.
 - Accomplished by completing online form, 90% from P2, remainder in narrative text.
- Notify MSC when Congressional member fact sheets are completed.

Major Subordinate Command (MSC) Program Manager (PgM)

5. Verify Performs quality assurance and approves Congressional member fact sheets.

If approved, goto task #8. Otherwise, goto task #6.

District Program Manager (PgM)

- Revise Congressional member fact sheet based on MSC feedback.
- 7. Notify MSC when Congressional Members' fact sheets are completed.

Major Subordinate Command (MSC) Program Manager (PgM)

Notify HQUSACE when Congressional Members' fact sheets are completed.

Headquarters (HQUSACE) Program Manager (PgM)

Performs quality assurance and approves Congressional member fact sheets.

If approved, goto task #10. Otherwise, goto task #6.


Copyright Oracle Corporation, 2000. All rights reserved.

Effective 07/23/01 Page 3 of 5 Rev 1

Civil Works Program and Budget Process-Section 4 USACE Project Management Business Process Manual PROC1030.DOC PROC1030

10. Submit fact sheets electronically to Congressional subcommittees.
End of activity.
Copyright Oracle Corporation, 2000. All rights reserved.

Civil Works Program and Budget Process-Section 4 USACE Project Management Business Process Manual PROC1030.DOC PROC1030 Effective 07/23/01 Page 4 of 5 Rev 1

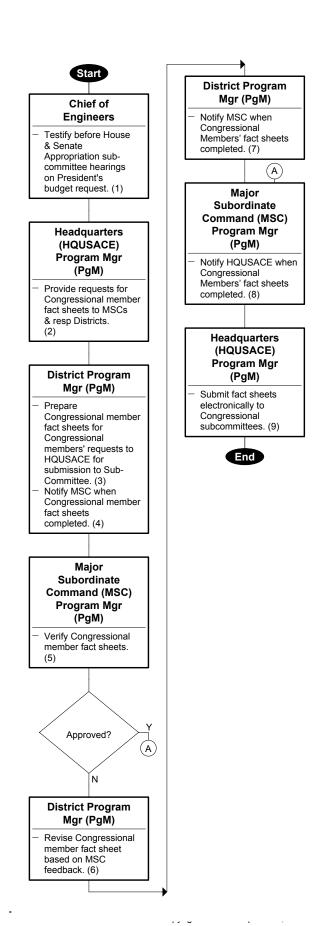

Civil Works Program and Budget Process-Section 4 USACE Project Management Business Process Manual PROC1030.DOC PROC1030

Effective 07/23/01 Page 5 of 5 Rev 1
