

Civil Works Program and Budget Process-Section 1 **Process 1027** Response: Accepted & Reworded. See master document

No NWD representative present while comments reviewed.

Scope

Prefer to retain PRISM and interface, rather than performing under P3e, in order to minimize data entry and continual system re-feeding. There is not sufficient confidence in the capabilities of P2 and P3e for the field to believe these processes will be efficiently implementable. Response: Rejected, Disagree that system will cause an increase in entry; being designed to reduce redundant data entry.

This process provides guidance for development and submission of the budget for the U.S. Army Corps of Engineers, Civil Works program.

- Saving a budget type in P3e will automatically trigger the P3e-Oracle Projects interface to pass “President’s Budget” budget-type to Oracle Projects. P2 will notify the Program Analyst that the “President’s Budget” budget-type has been sent to Oracle Projects.
- Once PM does recommended plan, then project is fit into ceiling, and adjustments need to be made back to PM.

Policy

EC 11-2-18x[<http://www.usace.army.mil/inet/usace-docs/eng-circulars/ec-cw.html>] (Note: The EC increases by one number each fiscal year. The EC includes a list of all applicable public laws, Executive orders, Army regulations, Engineer Regulations, Engineer Pamphlets, Engineer Manuals, and other policy guidance relevant to the budget year under development.)

Related Processes

Activity Development[[PROC1010](#)]

CEMRS Home Page[<http://www.usace.army.mil/inet/functions/rm/manpower/requirements/>]

Civil Works O&M Automated Budget System (ABS) Home Page[<http://www.cecer.army.mil/abs/default.asp>]

Civil Works Program and Budget Process[[PROC1022](#)]

Civil Works Program and Budget Process-Section 2[[PROC1028](#)]

Civil Works Program and Budget Process-Section 3[[PROC1029](#)]

Civil Works Program And Budget Process-Section 4[[PROC1030](#)]

Civil Works Program and Budget Process-Section 5[[PROC1031](#)]

District Operating Budget[[PROC1015](#)]

Initiating a Project in P2[[PROC1005](#)]

PMP/PgMP Content[[REF1018](#)]

Resource Estimate Development[[PROC1003](#)]

Responsibility

The Program Managers (PgMs) in HQUSACE, MSCs, and Districts are responsible for integrating and developing the Civil Works annual budget request, preparation of budget testimony, interfacing with Congressional committees, program/project management policy and guidance, and program management and performance.

The Project Manager (PM) is responsible for creating, updating and maintaining schedule/resource data consistent with guidance provided by HQUSACE.

The Program Analyst/Budget Analyst is responsible for creating appropriate budget types in P2, and preparing/updating PB-3’s (**Does HQ still require PB-3s?**) Response: Yes and PB-2a’s and District appropriation list per HQUSACE guidance The Project Review Board (PRB) is responsible for reviewing and verifying the appropriation list for accuracy and concurrence.

Distribution

Budget Analyst (BA)*
District Program Manager (PgM)*
Headquarters (HQUSACE) Program Manager (PgM)*
Major Subordinate Command (MSC) Program Manager (PgM)*
Program Analyst (PA)*
Project Manager (PM)*
Project Review Board (PRB)*

Ownership

The BP/P2 Program Office is responsible for ensuring that this document is necessary, that it reflects actual practice, and that it supports corporate policy.

Activity Preface

This process may be the first time a project is entered in P2 via *Initiating a Project in P2[PROC1005]*. This process runs concurrently with the PDT processes. The level of detail defined in *PMP/PgMP Content[REF1018]* will provide guidance for such items as activity/resource estimate development (refer to *Activity Development[PROC1010]*, *Resource Estimate Development[PROC1003]*.)

Headquarters (HQUSACE) Program Manager (PgM)

1. Release Civil Works Direct Program, Program Development Guidance Fiscal Year 20XX.

Major Subordinate Command (MSC) Program Manager (PgM)

2. Forward HQ guidance with supplemental implementation guidance to the District Program Management.

District Program Manager (PgM)

3. Provide HQ/MSC guidance with supplemental implementation guidance to the Project Managers.

Project Manager (PM)

If project is registered in P2, goto task #4. Otherwise, Stop and Complete *Initiating a Project in P2[PROC1005]*.

4. Make a copy of the current budget type of the project in P3e.
5. Update the copy consistent with MSC and HQ guidance and save as the "President's Budget Request".
 - Only projects in the budget will require budgetary types.
 - Refer to *Activity Development[PROC1010]* and *Resource Estimate Development[PROC1003]*.

Program Analyst (PA), Budget Analyst (BA)

6. Create additional budget version in Oracle Projects for copied budget types of each project, as needed.
 - This creates an initial set of budget versions of each project budget-type (President's Budget, Recommended, and Capability).
7. Verify PB-3's (?) and PB-2A's in Oracle Projects (for projects with CG funding only). **Note, both contingencies and actual work will need to be entered into system, at micro level. Currently contingencies can be accounted for at a macro level. Response: Contingencies are at both the project & program level.**
 - PB-3 will be updated at least once a year.
 - Run report for PB-3's and PB-2a's
8. Prepare General Investigation (GI), Construction General (CG), Operations and Maintenance (O&M) programs for district verification.
9. Verify project info for accuracy with previous budget guidance.
10. Run report listing studies and projects for each appropriation.

Project Review Board (PRB)

11. Review and verify list of studies and projects.
If list is verified, goto task #12. Otherwise, goto task #4.

District Program Manager (PgM)

12. Create Online Justification Sheets
13. Notify MSC of approved President's Budget, Recommended program, and Justification Sheets.


Major Subordinate Command (MSC) Program Manager (PgM)

14. Analyze and verify Division rollup of program data.
 15. Notify HQ of approved President's Budget, Recommended program.
- If program is approved, goto task #16. Otherwise goto task #2.**

Headquarters (HQUSACE) Program Manager (PgM)

16. Verify Corps-wide rollup of program data.
17. Lock Program data in OFA. **Define OFA.** Response: Reworded. See master document
18. Submit Program Memo to OMB through ASA(CW).

End of activity.

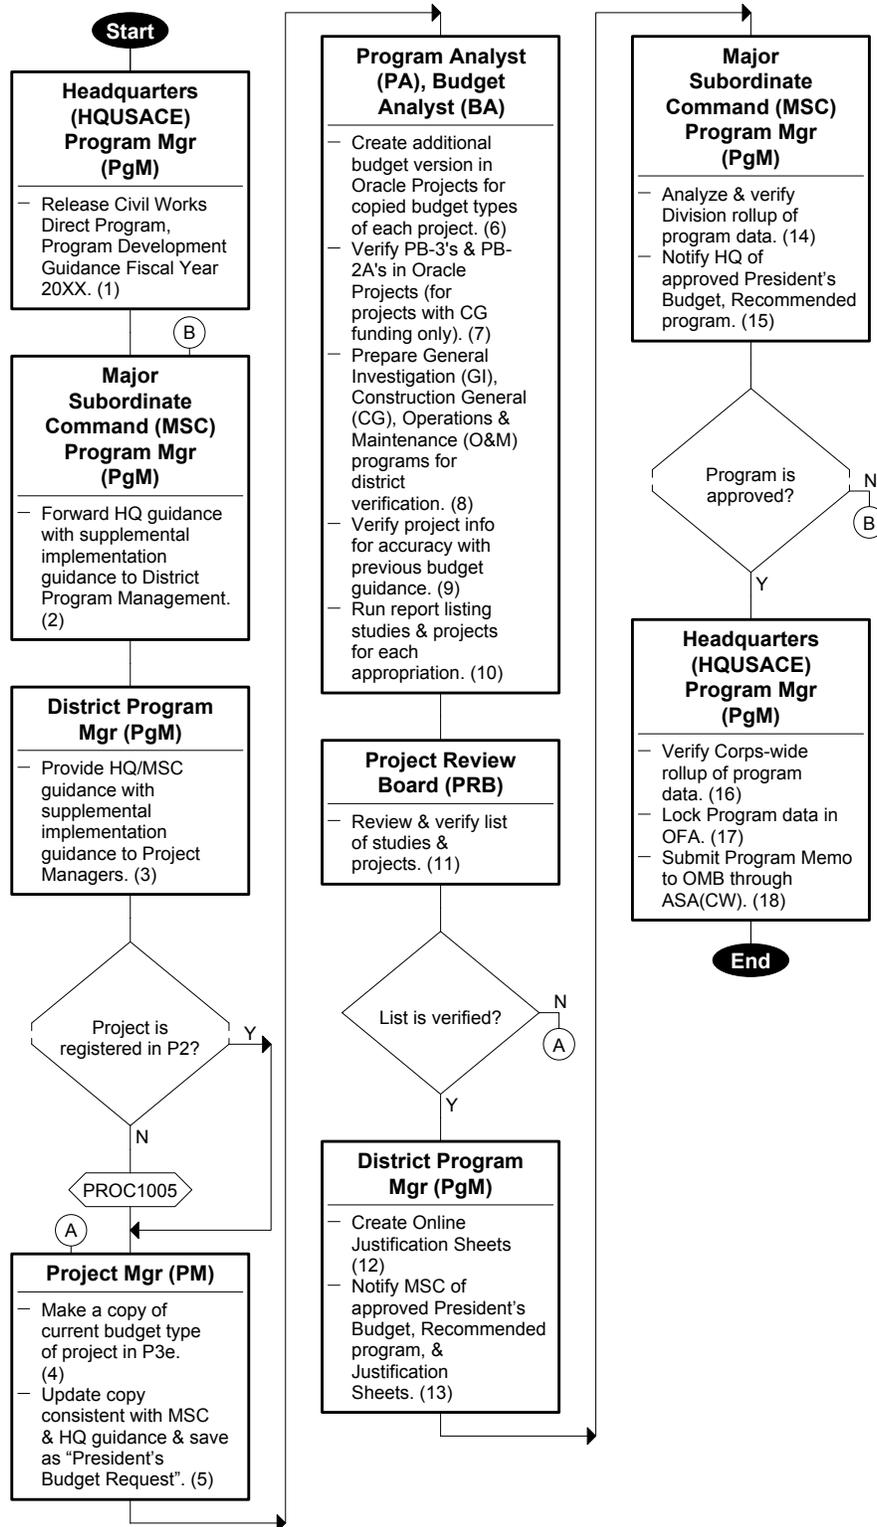

Civil Works Program and Budget Process-Section 1 Flowchart
